

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Mar 31, '19							Apr 7, '19				
							S	M	T	W	T	F	S	S	M	T		
1		Schedule Time Line	22 days	Tue 4/2/19	Wed 5/1/19													
2		Roofing	9 days	Tue 4/2/19	Fri 4/12/19													
3		Roofing : Bldg A (820/822) Front Elevation	2 days	Tue 4/2/19	Wed 4/3/19													
4		Roofing : Bldg B (816/818) Front Elevation	2 days	Tue 4/2/19	Wed 4/3/19													
5		Roofing : Bldg C (812/814) Front Elevation	1 day	Wed 4/3/19	Wed 4/3/19													
6		Roofing : Bldg D (808/810) Front Elevation	2 days	Thu 4/4/19	Fri 4/5/19	4,3,5												
7		Roofing : Bldg E (804/806) Front Elevation	2 days	Mon 4/8/19	Tue 4/9/19	6												
8		Roofing : Bldg F (800/802) Front Elevation	2 days	Mon 4/8/19	Tue 4/9/19	6												
9		Roofing : Bldg G (801/803) Front Elevation	2 days	Wed 4/10/19	Thu 4/11/19	7,8												
10		Roofing : Bldg H (805/807) Front Elevation	3 days	Wed 4/10/19	Fri 4/12/19	7,8												
11		Roofing : Bldg I (809/811) Front Elevation	3 days	Wed 4/10/19	Fri 4/12/19	7,8												

Project: Hunningdon II Schedule Date: Thu 4/4/19

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Mar 31, '19							Apr 7, '19		
							S	M	T	W	T	F	S	S	M	
12		Roofing : Bldg J (813/815) Front Elevation	3 days	Wed 4/10/19	Fri 4/12/19	7,8										
13		Roofing : Bldg K (817/819) Front Elevation	3 days	Wed 4/10/19	Fri 4/12/19	7,8										
14		Siding/Windows	3 days	Mon 4/29/19	Wed 5/1/19											
15		Window : Bldg B (816/818)	1 day	Mon 4/29/19	Mon 4/29/19											
16		Siding : Bldg A (820/822) Left Elevation	1 day	Tue 4/30/19	Tue 4/30/19	15										
17		Siding : Bldg B (816/818) Left Elevation	1 day	Tue 4/30/19	Tue 4/30/19	15										
18		Siding : Bldg C (812/814) Left Elevation	1 day	Tue 4/30/19	Tue 4/30/19	15										
19		Siding : Bldg E (804/806) Left Elevation	1 day	Tue 4/30/19	Tue 4/30/19	15										
20		Siding : Bldg F (800/802) Left Elevation	1 day	Tue 4/30/19	Tue 4/30/19	15										
21		Siding : G (801/803) Right Elevation	1 day	Wed 5/1/19	Wed 5/1/19	16,17,18,19,20										
22		Siding : H (805/807) Right Elevation	1 day	Wed 5/1/19	Wed 5/1/19	16,17,18,19,20										


Project: Hunningdon II Schedule
Date: Thu 4/4/19

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Mar 31, '19							Apr 7, '19			
							S	M	T	W	T	F	S	S	M	T	
23		Siding : J (813/817) Right Elevation	1 day	Wed 5/1/19	Wed 5/1/19	16,17,18,19,20											
24		Siding : K (817/819) Right Elevation	1 day	Wed 5/1/19	Wed 5/1/19	16,17,18,19,20											


Project: Hunningdon II Schedul
Date: Thu 4/4/19

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

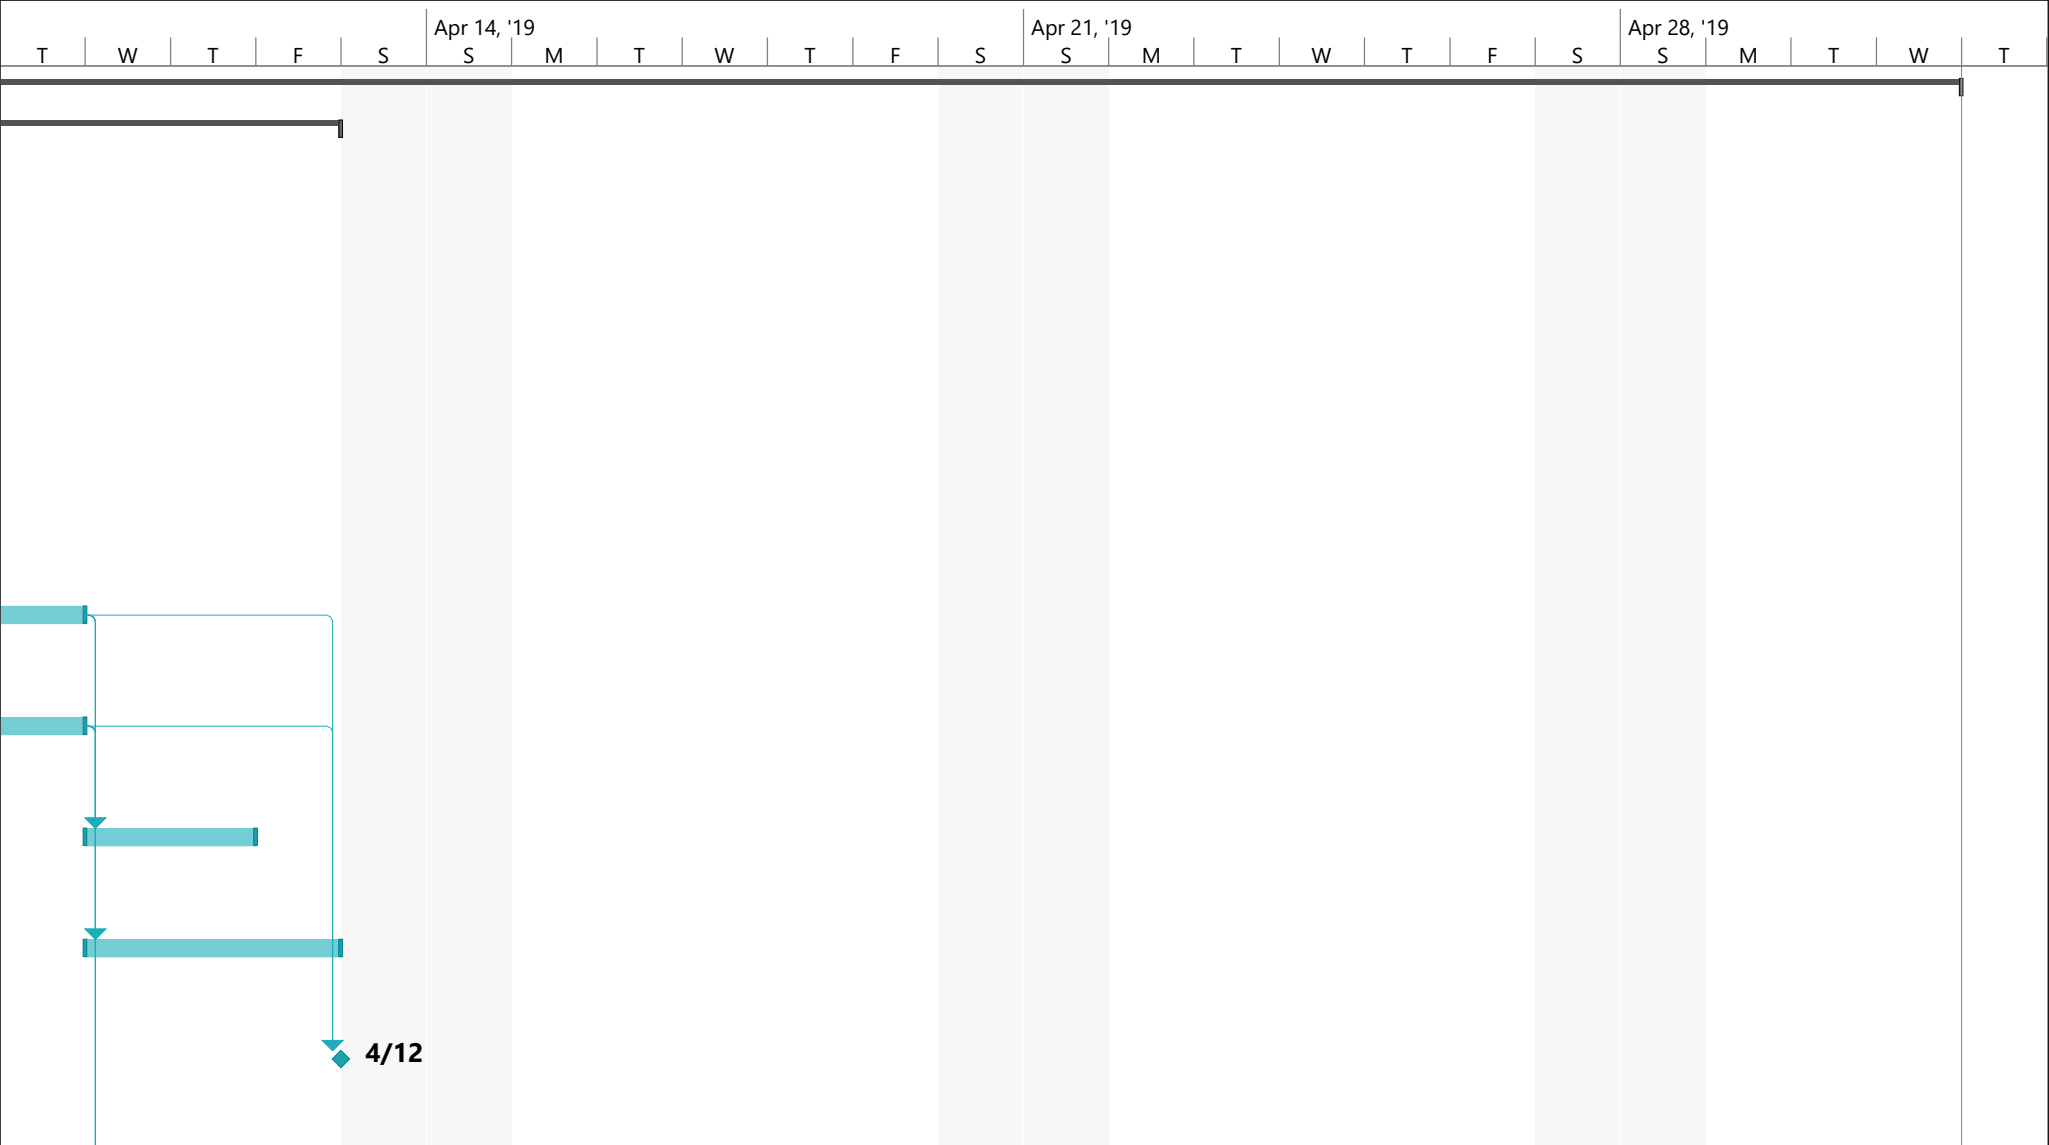


Project: Hunningdon II Schedul
Date: Thu 4/4/19

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

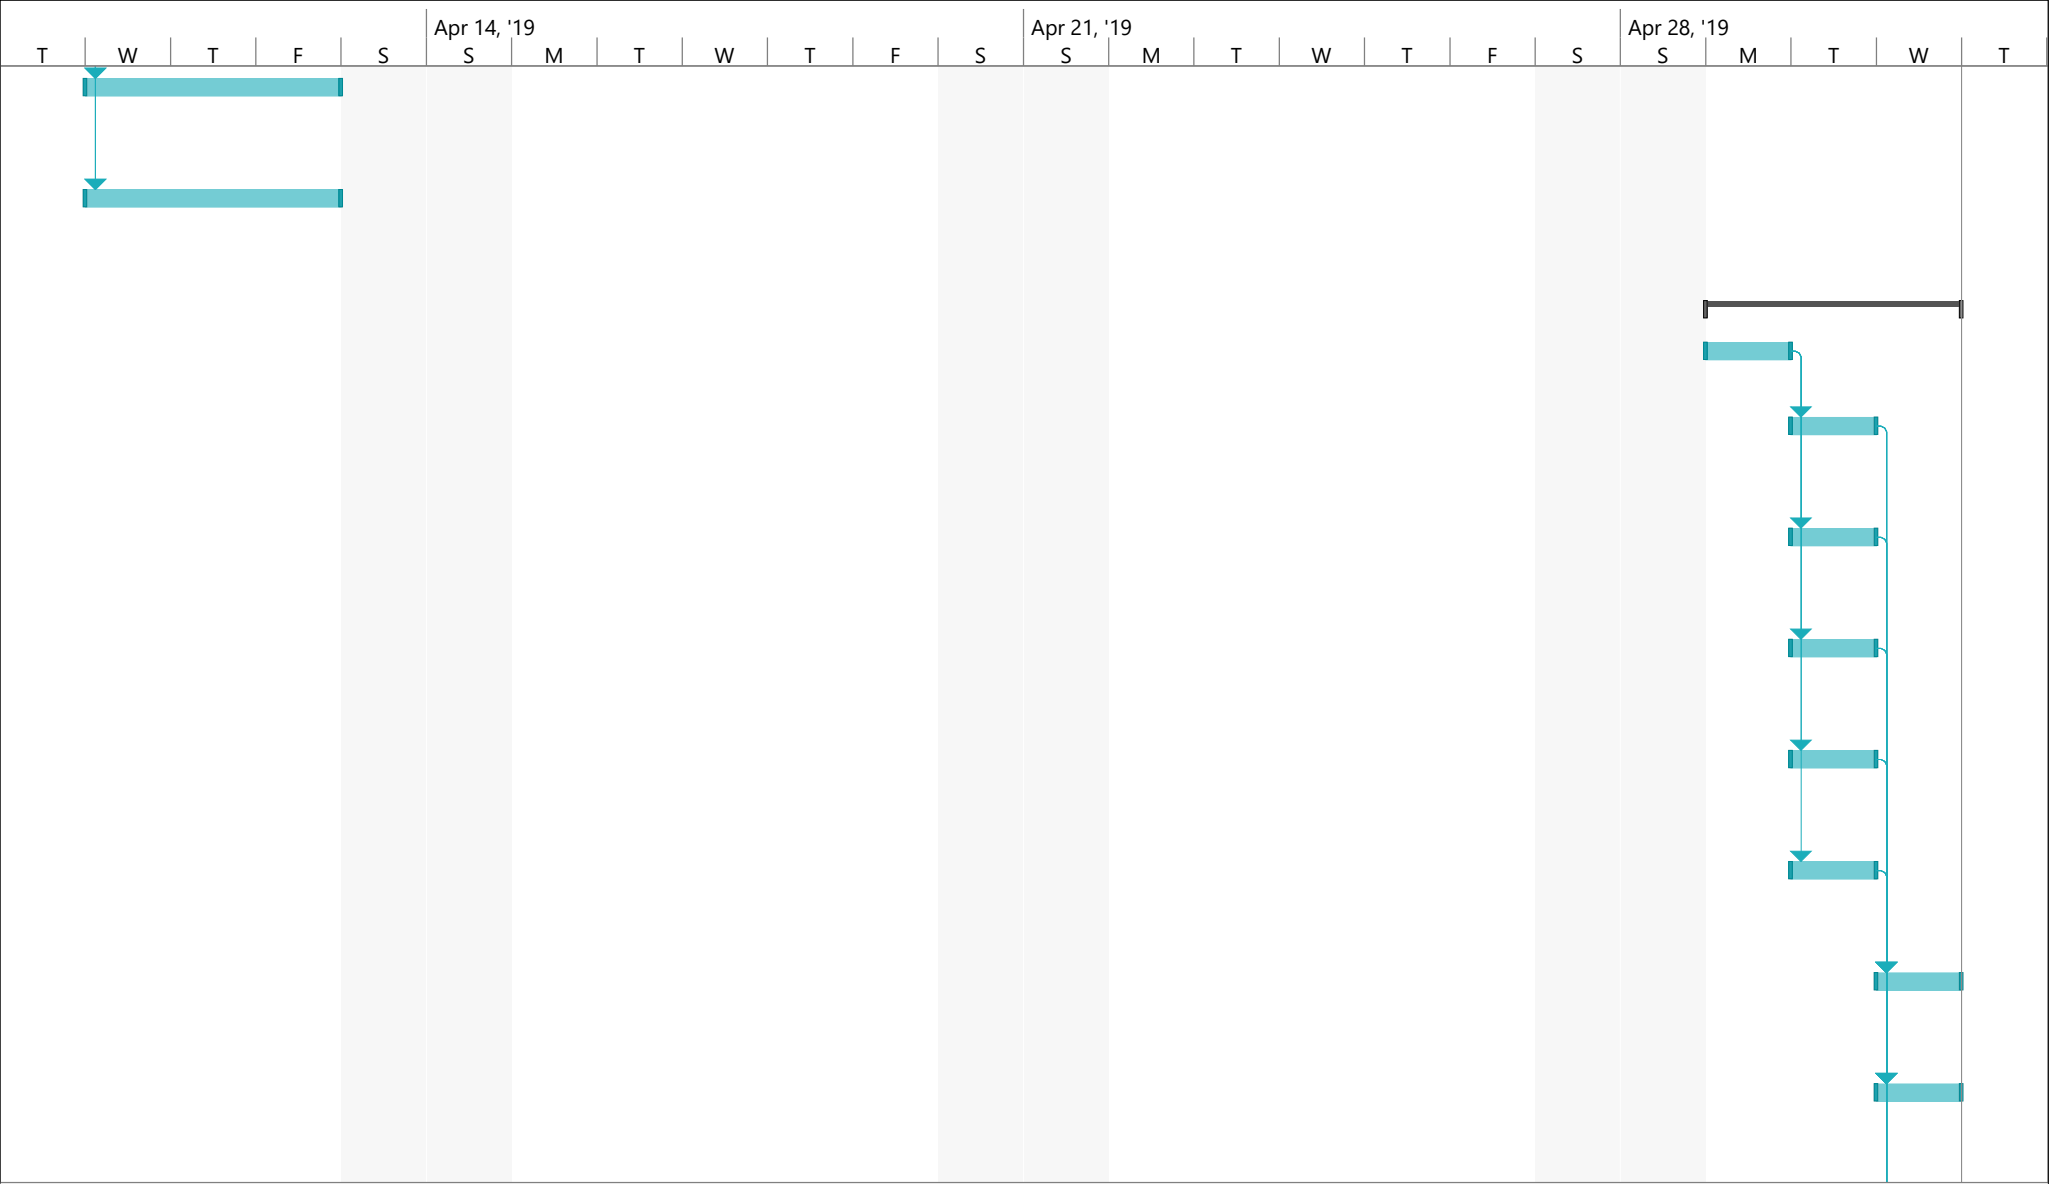

Project: Hunningdon II Schedul
Date: Thu 4/4/19

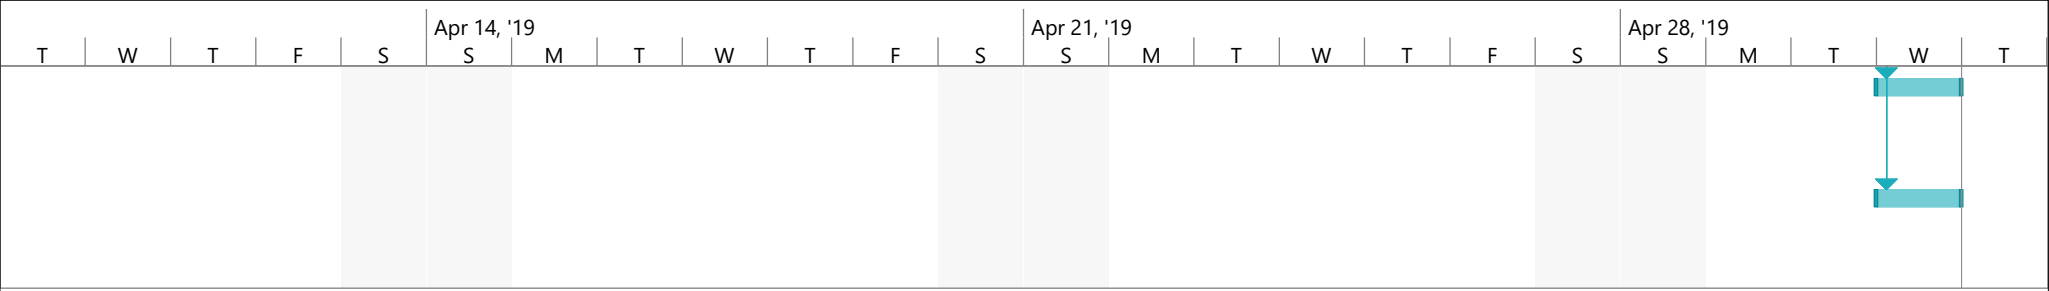

Project: Hunningdon II Scheduling
 Date: Thu 4/4/19

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			
